




TACLOUD

Launch Readiness and Project Handover Report

Final project review for production launch

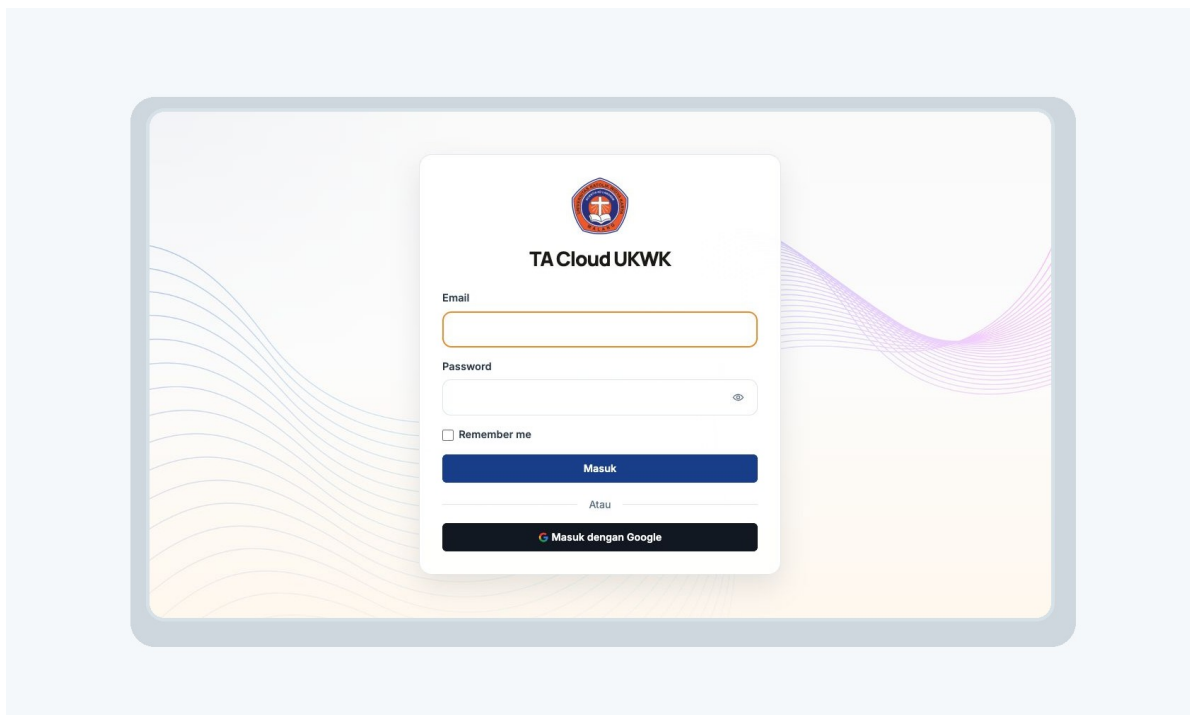

Prepared for

Head of Study Program (Kaprod)

Date

27 July 2026

Version

3.1

Recommendation

READY FOR A CONTROLLED PRODUCTION LAUNCH

Executive Summary

Launch recommendation TACLOUD is ready for a controlled production launch. No known issue currently prevents launch within the tested scope.

TACLOUD supports the thesis process from proposal submission to supervision, sidang, grading, final-document submission, completion, and public library listing. The application separates access for Kaprodi, Dosen, and Mahasiswa.

All 20 final test areas were completed. Seven accepted TestSprite browser tests passed. The current Laravel suite passed 135 tests with 457 assertions. Citra recorded all 38 manual QA checks as Passed.

Eleven Citra checks included remarks. The related paths were later fixed or technically verified. However, the same manual test was not repeated by Citra for every remark. This is recorded as an evidence limitation.

Readiness at a glance

Evidence	Result	Status
Final test campaign	20 of 20 scenarios completed	Passed
Accepted TestSprite tests	7 of 7 browser scenarios passed	Passed
Laravel automated tests	135 tests / 457 assertions	Passed
Focused workflow tests	22 tests / 90 assertions	Passed
Critical release suites	65 tests / 290 assertions	Passed
Authentication and import	39 tests / 175 assertions	Passed
Dependency audits	Composer: 0 advisories; npm: 0 vulnerabilities	Passed
Citra manual QA	38 of 38 recorded Passed; 11 with remarks	Passed with qualification
Known launch blocker	None within the verified scope	Clear

Conditions before launch

- Complete the production deployment checklist.
- Back up the database and private document storage, and confirm the rollback procedure.
- Use HTTPS, secure cookies, and HSTS at the server or reverse proxy.
- Run a short production smoke test for login, main role access, uploads, sidang, grades, completion, and library.

Document Contents

Section	Purpose
1. Project Overview	Purpose, users, scope, and expected outputs
2. Roles and Responsibilities	Access and responsibility by user role
3. How TACLOUD Works	Main thesis flow and role handoffs
4. Features Delivered	Delivered functional areas
5. Verification Method	How launch readiness was checked
6. Citra Manual QA	All 38 checks with clear explanations
7. Final Test Campaign	All 20 final test scenarios
8. Issues and Current Status	Important findings and remediation
9. Security and Production Readiness	Security controls and release gates

Section	Purpose
10. Launch Plan	Deployment, rollback, and monitoring

1. Project Overview

TACLOUD is a web application for managing the academic thesis process in one system. It reduces separate files, unclear status updates, and manual handoffs between Mahasiswa, Dosen, and Kaprodi.

Item	Description
Main purpose	Manage the thesis process from proposal to final publication.
Primary users	Kaprodi, Dosen, and Mahasiswa.
Public user	Can search and view information about completed theses.
Main outputs	Current thesis status, documents, guidance records, sidang requests, schedules, grades, completion records, exports, and library entries.
Authentication	Password login and institutional Google login for @widyakarya.ac.id accounts.

2. Roles and Responsibilities


Activity	Kaprodi	Dosen	Mahasiswa
Master data and periods	Manage	View when needed	View own context
Proposal	Review and decide	View assigned thesis	Create and upload
Supervisor and examiner	Assign	Perform assigned role	View assignment
Guidance	Monitor	Record guidance	View and upload revision
Sidang request	Approve or reject	Submit or cancel pending request	View progress
Grades	View recap and approve unlock	Enter, publish, and request unlock	View own grades
Final document	Review and complete thesis	View assigned thesis	Submit when eligible
Library	Monitor	Public access	Public access

3. How TACLOUD Works

Step	Responsible Role	Main Action and Result
1	Mahasiswa	Creates a thesis record and uploads the proposal.
2	Kaprodi	Reviews the proposal and approves or returns it for revision.
3	Kaprodi	Assigns supervisors and examiners.
4	Dosen and Mahasiswa	Record guidance, comments, revisions, and document versions.
5	Primary Supervisor	Submits the sidang request when requirements are met.
6	Kaprodi	Approves or rejects the request and sets the schedule.
7	Assigned Dosen	Enter and publish the required grades.
8	Mahasiswa	Uploads the final document after all required grades are available.
9	Kaprodi	Checks the final document and published grades, then completes the thesis.
10	System	Shows the completed thesis in the public library.

Important workflow correction The old Dosen final-document approval step was removed because it was not part of the required business flow. Completion now uses the latest final document and published grades from all assigned reviewers.

3.1 Main Role Handoffs

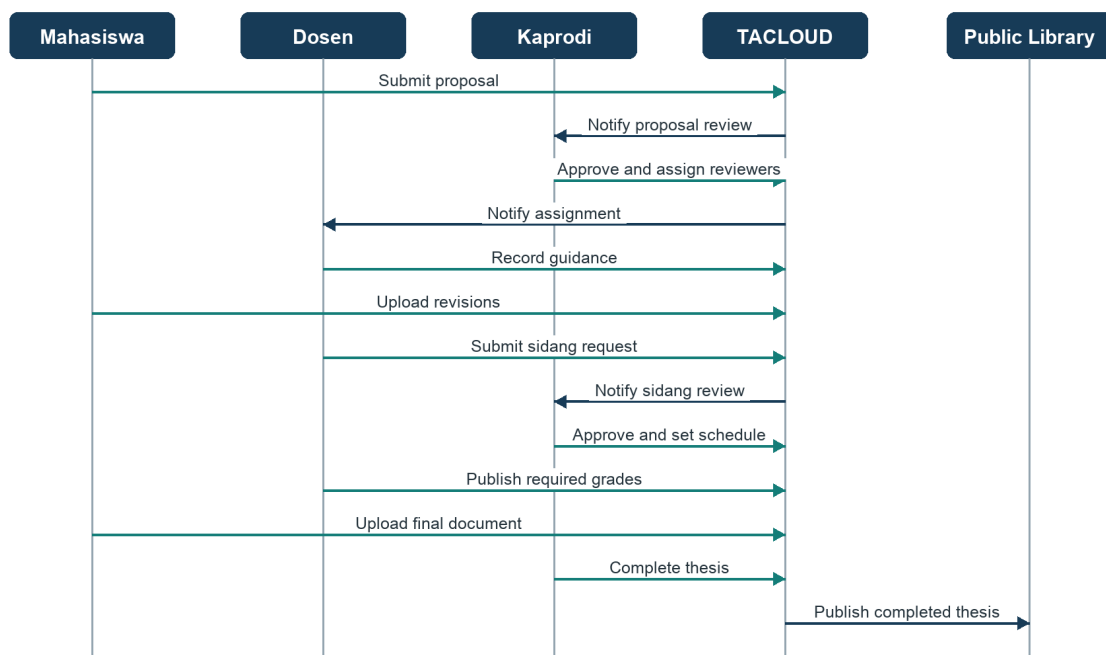

The diagram shows who starts each action and how TACLOUD passes the work to the next responsible role.

4. Features Delivered

Functional Area	Delivered Capability	Status
Authentication	Password login, logout, session protection, and institutional Google login.	Delivered
Master Data	Dosen, Mahasiswa, academic years, periods, grading formats, and CSV imports.	Delivered
Thesis Management	Owned thesis records, proposal review, assignments, phases, and monitoring.	Delivered
Guidance	Guidance notes, revisions, document versions, and logbook exports.	Delivered
Sidang	Requests, cancellation while pending, Kaprodi decision, and scheduling.	Delivered
Grading	Draft grades, publication and lock, recap, and controlled unlock requests.	Delivered
Final Documents	Eligibility checks, final upload, Kaprodi review, normal and historical completion.	Delivered
Document Templates	Required-document lists, period links, draft, publish, duplicate, and locking rules.	Delivered
Notifications	Personal notifications, read status, internal links, and realtime delivery support.	Delivered
Reports and Export	Thesis CSV, grade recap, monitoring, and guidance logbook export.	Delivered
Public Library	Search and detail pages for completed theses.	Delivered
Non-Thesis Records	Student management of abstracts, reports, scores, and publication links.	Delivered

5. Verification Method

Launch readiness was checked with several methods. Each method was used for the type of risk it can verify best.

Method	What It Verified
Citra manual QA	Real user tasks for Kaprodi, Dosen, Mahasiswa, and shared functions.
TestSprite browser tests	Accepted user flows in a real browser, including library, sidang cancellation, and the two-advisor sidang flow.
Laravel/Pest tests	Server rules, permissions, ownership, validation, files, security, workflows, and notifications.
Build and cache checks	Frontend build, route cache, configuration cache, view cache, and Laravel optimization.
Dependency audit	Known security advisories in Composer and npm packages.
Code and graph review	Current structure, affected files, workflow connections, and removed obsolete behavior.

6. Manual QA by Citra

Citra recorded all 38 checks as Passed. Eleven checks included remarks. The tables keep the original result separate from later technical verification.

Test Group	Total	Passed	Passed with Remark
Kaprodi	19	11	8
Dosen	7	6	1
Mahasiswa	7	6	1
General	5	4	1
Total	38	27	11

How to read the status Passed is Citra's original result. Passed with Remark means Citra recorded Passed but also described a problem or improvement. Current Status explains later evidence without pretending that Citra repeated every test.

6.1 Kaprodi QA

No.	Test Scenario	What Was Tested	Tester Result	Current Status
1.1	Dashboard	Dashboard widgets, counts, and statistics loaded correctly.	Passed	Verified
1.2	Program Study Master Data	Create, view, edit, and delete Program Study records.	Passed	Verified
1.3	Dosen Master Data	Dosen record management and CSV import.	Passed	Verified
1.4	Mahasiswa Master Data	Mahasiswa record management and CSV import.	Passed	Verified
1.5	Academic Year	Create, view, edit, and delete academic-year records.	Passed	Verified
1.6	Academic Period	Create, view, edit, and delete academic periods.	Passed	Verified
1.7	Grading Format	Create, view, edit, and duplicate grading formats.	Passed	Verified
1.8	Thesis Management	View the thesis list and open thesis details.	Passed	Verified
1.9	Reviewer Assignment	Assign supervisors and examiners to a thesis.	Passed	Verified
1.10	Proposal Review	Review, approve, or reject a student proposal.	Passed	Verified
1.11	Sidang Request Review	Review, approve, or reject a sidang request.	Passed with Remark	The tester saw an error after approval, although the status changed. The corrected flow is technically verified; an identical Citra retest is not documented.
1.12	Grade Recap and Unlock	View final grade recap and process grade-unlock requests.	Passed	Verified
1.13	Document Templates	Manage templates and connect them to academic periods.	Passed with Remark	The tester reported an error when reusing the same template. Validation and locking rules were later verified; an identical Citra retest is not documented.
1.14	Thesis Export	Export thesis data to CSV.	Passed with Remark	The tester reported an export error. A dedicated export route and menu were added and technically verified.

No.	Test Scenario	What Was Tested	Tester Result	Current Status
1.15	Final Documents and Library	Open the final-document queue and confirm library availability.	Passed with Remark	The tester found missing final-document requirements and an empty queue. The current completion-to-library path is covered by automated tests.
1.16	Sidang Schedule	Set the thesis sidang date and time.	Passed with Remark	The tester saw a database error. The required database field and route rendering were later verified; production smoke testing remains recommended.
1.17	Thesis Monitoring	Open thesis monitoring from the Kaprodi workspace.	Passed with Remark	The tester saw a Blade syntax error. The view was corrected and route rendering now passes.
1.18	Final Document Checklist	Save a checklist as draft and later publish it.	Passed with Remark	The tester reported that the status stayed Draft. Current draft, publish, and locking rules are technically verified; an identical Citra retest is not documented.
1.19	Final Document Monitoring	Open final documents waiting for Kaprodi review.	Passed with Remark	The tester saw a date-format error. The page and date handling were corrected; an identical Citra retest is not documented.

6.2 Dosen QA

No.	Test Scenario	What Was Tested	Tester Result	Current Status
2.1	Dashboard	Open the Dosen dashboard and assigned thesis queue.	Passed	Verified
2.2	Assigned Theses	View assigned theses and their details.	Passed	Verified
2.3	Guidance Records	Add, edit, and delete guidance notes.	Passed	Verified
2.4	Sidang Request	Submit, cancel, and submit a sidang request again.	Passed with Remark	The tester reported unclear feedback after submission. Laravel coverage and accepted TestSprite TC029 confirm cancellation and resubmission.
2.5	Grading	Enter grade items and publish the final grade.	Passed	Verified
2.6	Grade Unlock	Request an unlock for a published grade.	Passed	Verified
2.7	Notifications	Receive notifications for assignments, reviews, and requests.	Passed	Verified

6.3 Mahasiswa QA

No.	Test Scenario	What Was Tested	Tester Result	Current Status
3.1	Dashboard	View the active thesis, document count, and guidance summary.	Passed	Verified
3.2	Thesis Management	Create, edit, and delete an owned thesis record.	Passed	Verified
3.3	Documents	Upload proposal and document versions, then delete owned files.	Passed	Verified
3.4	Guidance	View guidance, respond to revisions, and export the logbook.	Passed	Verified
3.5	Final Submission	Open and submit the final-document form only after grades are available.	Passed with Remark	The tester requested an eligibility guard. Current automated tests confirm that early access and early submission are rejected.
3.6	Grades	View the student's own published final grades.	Passed	Verified
3.7	Non-Thesis Records	Manage an abstract, report, score, and publication link.	Passed	Verified

6.4 General QA

No.	Test Scenario	What Was Tested	Tester Result	Current Status
4.1	Authentication	Use valid and invalid login details and confirm role-based access.	Passed	Verified
4.2	Notifications	View realtime notifications and mark one or all as read.	Passed	Verified
4.3	Shared User Interface	Check shared page headers, cards, tables, forms, and icons.	Passed	Verified
4.4	Public Library	Open the public library list and thesis detail pages.	Passed with Remark	The tester reported that completed theses did not appear automatically. The corrected path is covered by five accepted browser tests and lifecycle tests.
4.5	FAQ and Limitations	Open the FAQ and Known Limitations pages.	Passed	Verified

7. Final Test Campaign

The final campaign covered 20 test areas. Passed means that the final verification found no launch-blocking issue in that area.

No.	Test Scenario	What Was Tested	Final Result
1	Test Environment and Data	Confirmed that the test database, migrations, accounts, roles, and sample data were ready.	Passed
2	Application Baseline	Checked the Laravel test suite, application routes, Blade pages, and frontend build.	Passed
3	Browser Test Setup	Confirmed that TestSprite could open TACLOUD and run the accepted browser scenarios.	Passed
4	Login and Session Security	Tested valid and invalid login, logout, rate limiting, session handling, and institutional Google accounts.	Passed
5	Role Access	Confirmed that Kaprodi, Dosen, and Mahasiswa can only access functions allowed for their roles.	Passed
6	Record Ownership	Checked that users cannot view or change thesis, guidance, or document records belonging to other users.	Passed
7	CSRF Protection	Confirmed that unauthorized form submissions without a valid security token are rejected.	Passed
8	Input Validation	Tested invalid and manipulated form data to ensure restricted fields cannot be changed.	Passed
9	File Security	Checked file type, upload path, ownership, thesis phase, preview, and download permissions.	Passed
10	XSS Protection	Tested whether harmful text or scripts could be stored or displayed through application inputs.	Passed
11	Search and Sorting Safety	Confirmed that search, filtering, and table sorting only use accepted values.	Passed
12	Browser Security Headers	Checked response headers used to reduce browser-based security risks.	Passed
13	Mahasiswa Workflow	Tested proposal management, document uploads, grade access, and final-document submission.	Passed
14	Dosen Workflow	Tested guidance records, grading, grade locking, and sidang request submission or cancellation.	Passed
15	Kaprodi Workflow	Tested proposal review, assignments, sidang approval, grade unlock, and thesis completion.	Passed
16	Complete Thesis Lifecycle	Confirmed that a thesis can move through the main phases and appear in the public library after completion.	Passed
17	Notifications and Privacy	Checked notification recipients, notification links, read status, and private data access.	Passed
18	Accessibility	Tested keyboard navigation, focus handling, modal dialogs, labels, and Escape-key behavior.	Passed
19	Production Routes and Cache	Confirmed that routes are unique and the application can build route and configuration caches.	Passed
20	Dependencies and Release Checks	Checked Composer and npm security reports, frontend build, optimization, migrations, and the final test suite.	Passed

Some scenarios found earlier defects or risks. The issues were corrected and tested again. The most important examples are summarized in Section 8; detailed evidence remains in the technical evidence package.

Accepted TestSprite Browser Results

Browser Test Group	Coverage	Result	Evidence Note
Public Library	Five browse, detail, and navigation scenarios	5/5 Passed	Accepted browser assertions
Dosen Sidang Cancellation	Cancel a pending request and submit it again	1/1 Passed	Laravel tests also verify the success message
Two-Advisor Sidang Flow	Both supervisors submit; Kaprodi approves; phase advances	1/1 Passed	Database and Laravel workflow evidence support the result
Old TC023	Removed Dosen final-approval workflow	Excluded	No longer represents the corrected business flow

8. Important Issues and Current Status

Issue Found	Action Taken	Verification	Current Status
The old final-document approval design could not reach normal completion.	Removed the unused approval model, UI status, tests, and database table. Completion now checks final documents and published grades.	Focused workflow and complete lifecycle tests passed.	Closed
Dosen sidang requests remained visible after submission.	Added clear pending-state handling, cancellation, and resubmission.	Accepted TestSprite TC029 and Laravel feature tests passed.	Closed
Unsafe shared-table HTML could allow XSS.	Escaped normal cell content and limited raw HTML to trusted action content.	Focused XSS tests and frontend build passed.	Closed
Unsafe sort direction could cause a server error.	Limited sort direction to accepted values.	Query-security tests passed.	Closed
Proposal upload accepted an incorrect document phase.	Restricted the endpoint to the proposal phase.	Upload and phase-validation tests passed.	Closed
A duplicate route name blocked production optimization.	Kept one main route name and renamed or removed duplicates.	Route cache and optimization passed.	Closed
Some Citra remarks do not have an identical manual retest.	Kept the original remarks and linked later technical verification.	Evidence is clear but not identical for every manual step.	Non-blocking evidence limitation
Developer test accounts and a predictable import password were present in production paths.	Removed the Akun Test shortcut and all runtime known credentials. CSV import now requires an explicit password of at least eight characters.	Fresh-install, authentication, import, full-suite, and reference-audit checks passed.	Closed

9. Security and Production Readiness

Control Area	Verified Result	Production Requirement
Authentication	Password and institutional Google login protections passed; no test-account shortcut or known production credential remains.	Use production Google credentials and HTTPS callback URLs.
Role and ownership	Cross-role access and record ownership tests passed.	Keep exact role middleware and current authorization checks.
Forms and input	CSRF, validation, mass-assignment, query, and sorting checks passed.	Do not disable middleware or validation in production.
Files	Type, path, phase, ownership, preview, and download checks passed.	Back up private storage and verify permissions.
Browser protection	Anti-sniff, frame, and referrer headers passed.	Enable HSTS at the HTTPS server or reverse proxy.
Dependencies	Independent live-registry audits on 27 July 2026 found 0 Composer advisories and 0 npm vulnerabilities.	Repeat audits before each release.

Control Area	Verified Result	Production Requirement
Build and cache	Vite 8.1.5 built 58 modules; route cache, configuration cache, views, and optimize passed.	Build from the approved release commit.
Session	Session controls passed in test scope.	Set secure cookies in production.

10. Launch Plan

Final recommendation Proceed with a controlled production launch after the checklist below is completed. This recommendation does not mean zero risk.

10.1 Deployment Checklist

- ☐ Freeze the approved release commit and record the application version.
- ☐ Back up the database and private document storage.
- ☐ Confirm that the backup can be restored.
- ☐ Set the production URL, database, mail, Google login, queue, and notification settings.
- ☐ Use HTTPS and secure session cookies.
- ☐ Enable HSTS at the server or reverse proxy after HTTPS is confirmed.
- ☐ Install production dependencies and build the approved frontend assets.
- ☐ Run database migrations and confirm their result.
- ☐ Seed production master data only; the verified seeder creates no users or known credentials.
- ☐ Create the first Kaprodi through institutional Google login, then promote only that exact account with a scoped operator command.
- ☐ Build Laravel configuration, route, event, and view caches.
- ☐ Start and monitor queue, scheduler, and realtime services where used.
- ☐ Run smoke tests for login, all three roles, uploads, sidang, grades, final completion, export, notifications, and library.
- ☐ Record the launch time, responsible person, and first monitoring result.

10.2 Backup and Rollback

Stage	Required Action
Before deployment	Create a consistent database and document-storage backup. Keep the previous application release.
Rollback trigger	Repeated server errors, failed login for a main role, migration failure, broken uploads, or data mismatch.
Application rollback	Return to the previous approved release, rebuild caches, and restart background workers.
Data rollback	Restore the consistent backup when a database migration or data change cannot be safely reversed.
After rollback	Check login, role access, record counts, documents, grades, notifications, and library entries.

10.3 Post-Launch Monitoring

Time	What to Monitor	Owner
First 2 hours	Login, server errors, migrations, queue, uploads, downloads, and response time.	Developer / Operator
First day	Proposal, sidang, grading, completion, notifications, and data consistency.	Developer / Kaprodi
First week	Error trends, failed jobs, storage growth, user feedback, and unusual access failures.	Developer
Second week	Review incidents and decide priorities for remaining non-blocking improvements.	Developer / Kaprodi

Appendix A - Evidence Sources

- TACLOUD current source code, routes, controllers, models, migrations, views, and feature tests.
- Code-review graph incrementally refreshed on 27 July 2026 with no errors.
- TestSprite_Final_Campaign_Evidence.md.
- TACLOUD_Current_Product_Flows_and_Roles.md.
- Citra public manual QA Google Sheet: 38 checklist rows.
- Local Laravel, Vite, Composer, npm, route-cache, and optimization results.
- Accepted TestSprite dashboard results and generated browser-test artifacts.

Appendix B - Evidence Limits

- Eleven Citra checks contain remarks. Identical manual retesting by Citra is not documented for every remark.
- The old TC023 result is excluded because the related Dosen final-approval workflow was removed.
- The TestSprite success-message assertion for Dosen cancellation was not present; Laravel feature tests verify the session feedback.
- HSTS and secure cookies depend on the final production HTTPS configuration.
- The Vite warning for /images/login-wave.jpg is non-blocking because the file is available from the public directory at runtime.
- Dependency audit results are time-sensitive. The report uses independent live-registry results from 27 July 2026 and audits must be repeated before release.
- Fresh-install proof used a disposable SQLite database: 57 migrations, zero users, four roles, one department, and two study programs. Shared MySQL was not reset.
- Never run migrate:fresh on shared hosting or production.
